	Task Name	Unit	Duration	Start	Finish	% Complete
1	Name of the work : Restoration and Improvements of Roads at Hesaraghatta Main road, G Ramaiah layout, Sai Archade layout, Vijaya bank layout, Adityanagara Phase-02, and Surrounding areas in ward no-03 of Yelahanka New town Sub-division					0%
2	Name of Agency: Sri K Venkataraju.					
3	Work Order No: BBMP/EE/YNK.D/EPMT-08/W.O/ Date: 15.02.2022					0%
4	Mobilization		10 days	Tue 15-02-22	Mon 28-02-22	100%
5	Earthwork Excavation for Drain Work	Cum	25 days	Sun 20-02-22	Thu 24-03-22	90%
6	Plain Cement Concrete 1:4:8	Cum	35 days	Fri 25-02-22	Thu 14-04-22	90%
7	TMT Steel	Tonne	35 days	Sat 05-03-22	Thu 21-04-22	90%
8	Reinforeced Cement Concrete M20	Cum	40 days	Thu 10-03-22	Wed 04-05-22	90%
9	100mm Precast Covering Slabs	Sqm	35 days	Fri 25-03-22	Thu 12-05-22	90%
10	230mm Culvert Covering Slab	Sqm	35 days	Fri 25-03-22	Thu 12-05-22	90%
11	Plain Cement Concrete 1:3:6	Cum	35 days	Mon 28-03-22	Fri 13-05-22	90%
12	Pre Cast Kerb	Nos	45 days	Mon 28-03-22	Fri 27-05-22	100%
13	Earthwork Excavation for Road Work	Cum	35 days	Tue 15-03-22	Mon 02-05-22	80%
14	Compaction of original ground	Sqm	35 days	Sun 20-03-22	Thu 05-05-22	80%

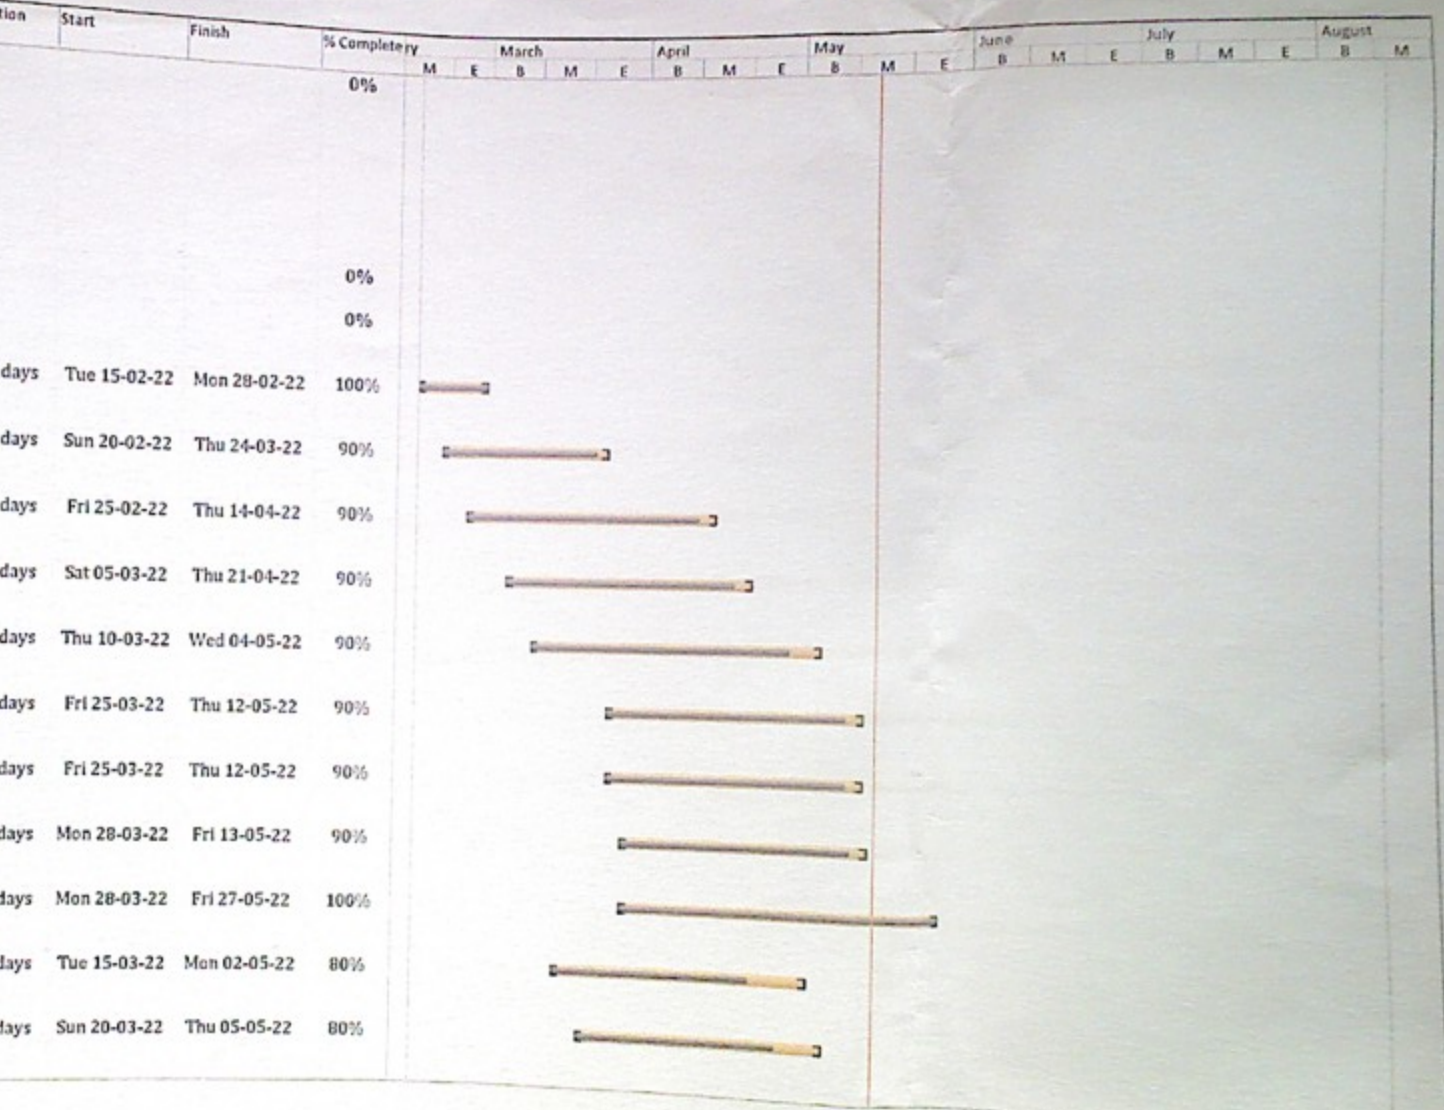

Project: Package-09, Bar Chart
Date: Sun 15-05-22

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress

W03 AE

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ.

of Government materials supplied

Net Amount

Contractor's Signature

	Task Name	Unit	Duration	Start	Finish	% Complete
15	Granular Sub Base	Cum	50 days	Fri 25-03-22	Thu 02-06-22	80%
16	Wet Mix Mecadam	Cum	50 days	Wed 30-03-22	Tue 07-06-22	80%
17	Primer Coat	Sqm	55 days	Sun 10-04-22	Thu 23-06-22	80%
18	Dense Graded Bituminous Macadam	Cum	70 days	Mon 11-04-22	Fri 15-07-22	80%
19	Tack Coat	Sqm	70 days	Tue 12-04-22	Mon 18-07-22	80%
20	Bitumious Concrete	Cum	70 days	Wed 13-04-22	Tue 19-07-22	80%
21	Lane Marking	Sqm	25 days	Sun 10-07-22	Thu 11-08-22	50%
22	Pavement Markers or Studds	Nos	25 days	Sun 10-07-22	Thu 11-08-22	50%
23	Kerb Painting	Sqm	30 days	Fri 01-07-22	Thu 11-08-22	50%
24	Dry Lean Cement Concrete (DLC) for CC Road	Cum	25 days	Sun 19-06-22	Thu 21-07-22	0%
25	Kerb Painting	Sqm	35 days	Sat 25-06-22	Thu 11-08-22	0%

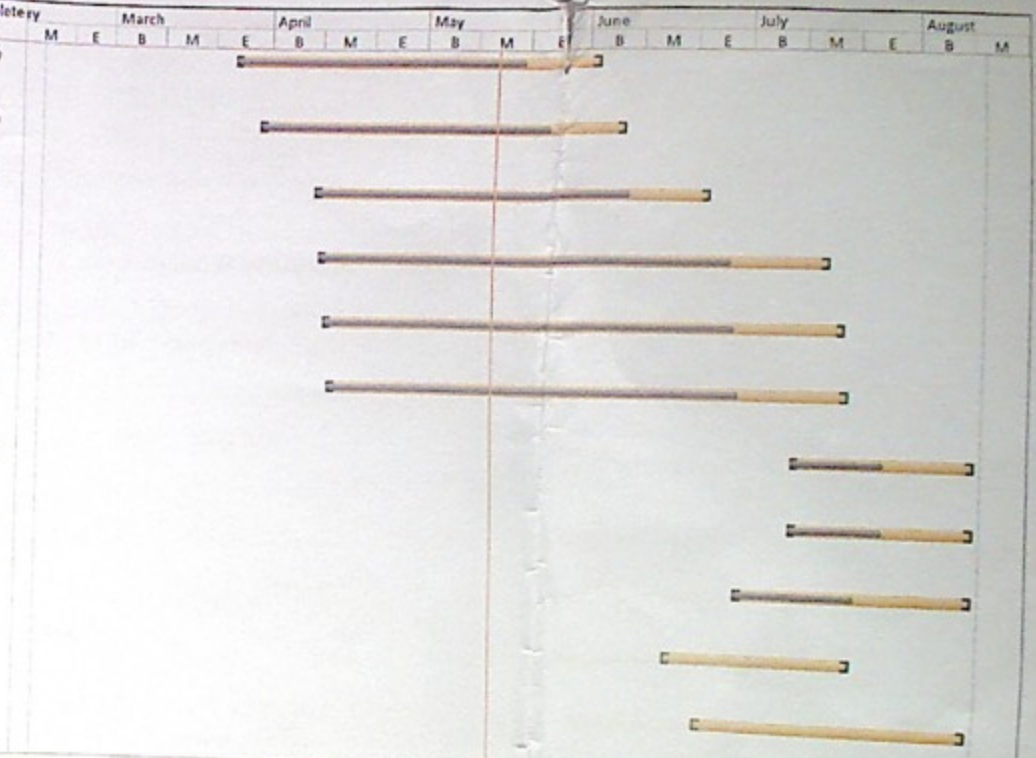

Project: Package-09, Bar Chart
Date: Sun 15-05-22

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ
ಯಲಹಂಕ ಉಪವಿಭಾಗ ಸಹವಿಭಾಗ.
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-10ನೇ

W-03 AE
